G. R. S. 59]

GPB—15,000– 20 12 13

GENERAL AND REVENUE SECRETARIAT.

1898–1899.

~~191~~ .

(Madras)

File No. 45

Serial Nos. 1–27

Papers Filed.

Month ~~August~~ 1904.

SUBJECT.

Repairs to the Sri Chennakes
Swami Temple at Bagur in the
Sub Taluk.

PREVIOUS REFERENCES.	LATER REFERENCES.
Mutg 7. 83-94.	Mutg 7. 246-12.

MYSORE : DEWAN'S OFFICE.

MUZRAI BRANCH.

OFFICE NOTE

SUBJECT — Repairs to the Chenna Kesavaswami Temple at Bangur in Hosdurga Sub-Taluk.

LAST REFERENCE. — Letters Nos. 5487/1456 ~~dated~~ & 1076/805 ~~from~~ dated 23rd April and 26th June 1901, from the Comptroller to the Govt. of Mysore and the Dy. Commr., Chitradurg Distt respectively.

In Govt. Lr. no 312-3 dated 20th September 1894.

In September 1894, an Estimate for Rs 1663 was sanctioned* for repairing the Sri Chenna Kesavaswami Temple at Bangur, the charges being met as suggested

below :—

Rs 171-5-10 From Temple Savings.

Rs 500-0-0 From Contributions

Rs 991-10-2 From the State Grant for 1894-95.

Total 1663-0-0.

The works sanctioned in the above order were not executed till about 1898, when the Dy Commr submitted a revised Estimate amounting to Rs 3769, providing therein for some additional works since found necessary. The original Estimate was thereupon cancelled and the

In Govt Res no 675-6

dated 8th Dec: 1898

The revised Estimate

sanctioned*, the charge

being met as follows.—

Rs 393-12-10 Temple Savings

Rs 500-"-" Contributions

Rs 2875-3-2 } out of State Grant for 1898-9

3769-"-".

In his Letter no

24H / 20H dated 13th September 1900

The Dy Comr again

reported, Govt in the

course of the execution of

work some additional

work was found necessary

& Govt he undertook the

additional work also

and very nearly completed

it. He also submitted an

for formal sanction

revised Estimate

below :—

Rs 171-5-10 From Temple
Savings.

Rs 500-0-0 From Contributions

Rs 991-10-2 From the State
Grant for
1894-95.

Total 1663-0-0.

The works sanctioned
in the above order were
not executed till about
1898, when the Dy Commr
submitted a revised Estimate
amounting to Rs 3769,
providing therein for some
additional works since
found necessary. The
original Estimate was
thereupon cancelled and
the

The revised Estimate

*: In Govt Endo no 675-6 dated 8th Dec: 1898 sanctioned, the charge being met as follows:—

Rs 393-12-10 Temple Saving
Rs 500-"-" Contributions
Rs 2875-3-2 } out of State Grant for 1898-9

3769-"-".

The Dy Commr again reported Govt in the course of the execution of work — Some additional work was found necessary & Govt be undertook the additional work also and very nearly completed it. He also submitted a revised Estimate for formal sanction:

⊗ In his Letter no 24 / 20 dated 13th September 1900

amounting to Rs 7557,
and added thereto out of this amount
Rs 3608 have to be newly
sanctioned from the State
Grant as per details noted
below :—

	Rs as P.
Amount of the sum revised Estimate	7557—0—0
Deduct amount already sanctioned in Govt Lrs No 675-6 dated 8th December 1898.	3769—0—0
Balance	3788—0—0

Deduct amount of temple savings since accumulated Rs 80—0—0	
And the amount since contributed by Votaries 100—0—0	
	180—0—0
Balance to be sanctioned from the State Grant	3608—0—0

In reply, the Dy Commr
was asked to report how much
of the allotment of Rs 3769
sanctioned in the Govt
order of the 8th December 1898,
had been drawn by him in
advance and expended
on the repair of the Temple,
and to submit measurement
lists for works already
executed under the original
Estimate. The Dy Commr was
also requested to report, with
reference to the revised
Estimate (for Rs 7557),
what items of work provided
for therein had been actually
carried out and what are

In his Office
Docket no 611 dated
3rd December 1900.

Cost, and what ~~other~~
items remained to be exe-
-cuted.

In reply to the above,
the Dy Commr in his Letter
No 608 dated 25th January 1907,
reported that he had drawn
an advance of Rs 3764 and
submitted measurement-
bills with Vouchers in support
of the Charges. He also reported
that more than 90 per cent
of the work provided for
in the second revised estimate had
been executed, but it
had not been measured
and paid for for want
of funds and that the

many ~~other~~ noted

marginally noted items of work remained to be done.

Thereupon the Comptroller was asked to report what payments were still outstanding in the accounts as advances pending adjustment, what payments had been finally adjusted and to what particulars thereof each payment had been debited.

With reference to the above the Comptroller submitted a statement, wherein it was noted

(1) Plastering walls and over concrete

(2) Painting compound wall

(3) Fixing coping slabs over the same

(4) Repairs to floors

(5) Separation of doors and windows.

as noted in the margin*

That 3 items were kept

under objection and all

other advances adjusted;

and on being asked,

in his office Docket no 1017

dated 25th March 1901,

why these three items were

under objection, he now states

in his Letter no 5487/1456

dated 15th April 1901,

that completion bills are

required for these 3 items

and (the state grant of

1898-99 having been lapsed)

the re-sanction for the

last 2 items to debit them

to the State-grant (of the

Official year) is also necessary.

Rs	as	P
128	2	6
132	4	"
1166	"	4
1426	6	10

The Dy Commr has now submitted a reminder to his Letter no 244 dated 12th September 1900, soliciting sanction to the revised Estimate amounting to Rs 7557. He has also sent an Explanatory memo noting down the items of work according to the original and the revised estimates.

What is now required to be done on the communications of the Comptroller and the Deputy Commissioner is :—

To accord re-sanction of Government to the

The marginally-noted two items to the State grant for 1901-02

Rs 132-4-0
1166-0-4
1298-4-4

ii To forward the completion bills already received from the Dy Comr to the Comptroller for adjustment.

And III, to sanction the revised Estimate amounting to Rs 7557, the excess charge viz Rs 3608 being met from the State-grant for 1901-902.

Submitted
Instead of sanctioning the revised Estimate now read, it would be convenient to call for a supplimental Estimate and then sanction it.

Submitted for orders

Rs
29/6/01

Sanction Rs. 1298-4-4 from the State grant for 1901-02 and send off the completion bills to Comptr. For the rest, call for a supplemental estimate HH 29/6/01

Note Continued :—

With ref^ce to the Dy Leg^s orders of 29th June 1901, the 11 measurement Bills aggregating Rs 3764 on account of repairs executed to the Sri Channakesavaswami temple at Bagur were passed and forwarded to Comptr for adjustment and the Dy Commr was requested to submit a supplemental Estimate for other ~~other~~ works already executed in anticipation of sanction.

Vide Govt Ro: No 53-4 mwz 745-98 dy 8th July 1901

The Dy Commr now reports that Rs

the Sanctioned Estimate
of Rs. 3769, work of the
value of Rs. 4564-1-5
has actually been carried
out for which Rs 3769
has been paid to the Contractor
and that Rs 795-1-5
still remains to be paid.

The Dy Commr also
submits ~~for sanction~~
a Supplementary Estimate
amounting to Rs 3251
for work still required to
be executed and requests
sanction thereto to enable him
to carry out the repairs
before the monsoons set in

Submitted for orders

5th March 1902

[illegible]

What are the items of work that have been executed and what are the items that have yet to be done? If the latter are not of an urgent nature, they cannot be undertaken now as much money has already been spent on the temple without due authority. HH 11/4/02

I find that for work actually executed, a further sum of Rs. 795-1-5 is still due. Sanction that amount at once from the Stale grant of this year. Ask the Dy Comr not to start any more work without obtaining prior sanction. HH 2/6/02

Note continued

The above order was communicated to the Deputy Com. in Govt Pro No 2002-3 dated the 6th June 1902 (Mukt 45-98) In reply, he submits this [illegible]

Memoranda, — one shewing the works already done to the temple, and the other, those remaining to be executed, to complete the repairs undertaken With reference to the latter, the Deputy Comr states that on a personal inspection of the temple, he is of opinion that the works enumerated therein are all essential, and accordingly submits a Supplemental Estimate therefor for Rs 3137/- for sanction

If this Estimate be sanctioned, the whole amount will have to be met from the State Grant of the current Official year.

— Subd
GA
13.9.02.
JS

Already work to the extent of Rs 4564-1-5 has been executed to the temple and paid for, the greater

part of which was from the State grant — A further sum of £6.3/37/- is now asked for from the State Grant for work still to be done — It is impossible to give such a large grant to this temple alone this year. The State grant is not intended to cover the purposes of merely one or two institutions in the State but of all that are in need of Govt aid. I therefore the Manr will send up a fresh estimate for work actually required to make secure the work actually already done, the proposal will be considered by Govt — and not otherwise

Inform Dr/- accordingly

22/9/02

Note continued

The above orders were Communicated to the Dy Comr

in this office no. Tour 745-98
dated 29th Sept. 1902. In
reply, he submits a detailed
Estimate for Rs 2830 for
such items of work as are
absolutely necessary to secure
the safety of the works already
executed as well as to ensure
the stability of the building
in general.

The amount of the present
Estimate is Rs 307 (3137-2830)
less than that of the Estimate
last submitted by the Dy
Comr.

Submitted.
Comm 13.1.03.

Deputy Secretary's remarks.

This is one of the temples on which much expenditure has been incurred by local Officers without obtaining the previous sanction of Government. The estimate commenced with Rs. 1663 in 1894 and went on increasing until it reached Rs. 3769 in 1898. Up to this Mr. Srinivasacharlu gave the necessary sanctions. Subsequently in September 1900,. Mr. M.S.Narayana Rao (Deputy Commissioner) raised the estimate to Rs. 7557 and reported that most of the additional work was nearly completed. Mr. Srinivasacharlu pointed out the highly irregular nature of the Deputy Commissioner's action, and asked for certain particulars.

After I took charge, owing to an objection raised by the Comptroller that the Deputy Commissioner had drawn and paid moneys connected with the estimate after they had lapsed, I had to give renewed sanction to a sum of

Rs. 1298 - 4 - 4, and a further sum of Rs. 795 - 1 - 5 for paying up the contractor for work actually done up to that date. These payments were defrayed from the State Grant of the past year 1901-1902. Having thus settled the accounts so far, I requested the Deputy Commissioner not to start any more work on the temple without obtaining the previous sanction of Government.

In September 1902, a suppemental estimate for Rs. 3137 was received from Mr. M. Narayana Rao (Deputy Commissioner) who pointed out that work to that extent was absolutely necessary in order to complete the repairs already effected and that on personal inspection he thought that the proposed works were essential. I replied that the State Grant was not intended to serve the purposes of ~~nearly~~ merely one or two Institutions in the State, but of all that are in need of Government aid, and requested the Deputy Commissioner to send a small

estimate for such of the works as are actually required to make secure those actually already done to the Institution. The result is that the estimate is reduced by the small sum of Rs. 307 and submitted for a sum of Rs. 2830.

Under the foregoing circumstances there seems to be no help for it but to sanction this supplemental estimate for Rs. 2830, as the additional woks are reported to be absolutely necessary. Out off the State Grant for the current year a sum of Rs. 4000 is still unutilized, and out of this the present estimate may be sanctioned, but only Rs. 1500 given for this work from this year's grant, the balance being deferred for disposal next year. What still remains out of the year's grant (viz. Rs. 2500) is required for other equally important works which will be brought to notice.

This case illustrates the necessity for checking the propensity of

Deputy commissioners to incur expenditure of large sums of money on their own authority without obtaining the previous sanction of Government. The State Grant of Rs. 15000 has to be distributed by Government over a great many Institutions in the State, and it causes much inconvenience to Government to get all at once without previous notice a large bill for some thousands of rupees for works undertaken and executed by a Deputy Commissioner without previous Government sanction.

A draft circular to Deputy Commissioners on the subject is submitted for approval.

Subd. to the Dewan
20/5/03.

Dety 10399
21 5 03

Read & take
what are the
works said
to be absolutely
necessary

22 V.03

Submitted 21-5-03

Back from Dft ask the Govt. Counsel
for information
27/5/03
12-4-03

Note Continued :-

The Dy Commissioner

Mr Ramanujiengar, who was

entrusted on the subject, inspected

the temple twice and has submitted

revised

3 Estimates amounting in all to Rs

17 40 in lieu of the original Estimate

for Rs 2830. He says that every

item of the Estimate was subjected

to the most careful scrutiny in

consultation with the Shanbhogs

and others interested in the temple.

The estimated cost, if sanctioned

will have to be met from the State

funds of the current Official

year.

Submitted

Ks

6/8/04

with his
Letter 63/405
dated 28th
July 1904.

The Estimates having
now been reduced from
Rs. 2830 to Rs. 1740, it is
submitted that the last
named amount may be

be sanctioned and the three revised Estimates passed. The present Dispatch has been the simple tenor and has given the assurance that the estimates cannot be reduced any more

Theodore Roosevelt
6/8/04
Camp Roosevelt

Send to the Treasury through the 2nd Lord

No 50
8 Aug 04. Mr Secretary
Revised estimates
may be sanctioned
Mr Secretary's
and I do recommend
to your approval any expenditure
beyond his powers of expenditure
for purposes mentioned
in these revised estimates
of last year.

Yours truly
15. VIII 04

901
11. VIII. 04

Recd 11/8/04

Recd 5 p.m.
JS
16/8/04

Put up draft TH 17/8/04

(General Serial No. 30.)

1897.98.

From The Deputy Commissioner
Chitaldroog District.

To

The ~~Chief~~ Secretary to the ~~Govt~~
Government of Mysore

Dated 1st Inungarai Departt:
Despatched 5th "
Received } July 1898.

OFFICE OF THE DEWAN OF MYSORE
RECEIVED
Date 7-7
PEG No 15
MUZRAI BRANCH

Enclosures No 3.

See General No. 1-
No. 1-

In reply to

SUBJECT

Submitting for sanction Revised Estimate of the probable cost of repairing Chunakesavaswamy's Temple at Bagur in the Holadurga Range, Holal=ker Taluk.

Refers
2-2 W

Ack to be done
& Sketch &c Cole
Cn

References (to be entered only in the Dewan's Office),

No. 1- Eu: 3-

Deputy Commissioner's Office
Chitaldrug District
Dated 1st July 1896

To,

The Secretary to the
Government of Mysore
Revenue Department

Sir,

With reference to your docket No. R-2 dated 19th October I have the honor to state that the contributions paid by the villagers of Bagur in the Hosadrug Sub-Taluk amounting to Rs 500 was paid into the Holalkere Taluk Treasury on the 27th December 1895 The Treasury Officer's Certificate as to the amount of savings at the credit of the contribution is herewith forwarded

2 On making a detailed inspection of the Temple in March last I found that some items of work

P.T.O.

not provided for in the estimat
sent by my predecessor e
were necessary. These have been
included in a revised estimate
here with submitted. There is
Concrete roofing over the temple
has been broken up and has to be
replaced. The Compound
wall has been built and
without stone slab at top
in place of Chunam Coping
the wall will be damaged
Along with these works and
the doors re necessary I have
provided for a little improve
ment to the mantap on both
sides of the entrance to serve
as a Kitchen and a yagasala
which are absolutely necessary
I beg therefore that the
Revised estimate now sent

may be sanctioned and the necessary allotment made for expenditure in 1898-99.

I have the honor to be
Sir,
Your most obedient Servant

Deputy Commissioner

MUZRAI

~~189~~ 1898-9

From

To The Dy Comm.r
Chitaldrug District

Dated 13 July
Despatched 14
Received
General No. 97
Muzrai F. No.

Enclosure No. 3

His letter no. 1 dy 1st
July 1898 submitting for
sanction a Revised
Estimate for repairing
the Sri Channakesava
Swami temple at Bagur
in the Hosadurga Sub Taluk.

With reference to the
above has the honor
to request that a
sketch of the temple
premises and the
portions now required

From the Tahsildar no 3-3/15

& ue reported
may be prepared & submitted
~~furnished~~ to this Office for reference
~~at an early date.~~
2. Enclosed for reference re-indorsement with the
Sketch above called for

By order

A.A.

Mus. Leg.

AAA

Gen. 31

1898/99 Gl 3

From The Deputy Commr
Chitaldrug Dist.

To The Secretary to the
Govt. of Mysore
Muzrae Dept.
Bangalore

Dated 12th October 1898.
Despatched 13th

Received

General No. 323-
No. 15-

Ref. 1040



Refer as
15 10 98

Seen Sir
11
Ol
11 12 98

His docket no: 97 dt 13th July last returning the revised Estimate for resubmission with a sketch of the temple premises and the portion now proposed to be repaired &c. -

---

With reference to the above, has the honor to resubmit the revised Estimate for repairing the temple &c.

To Hd. Samo no 675-6 4/5

of Sree Chenna Kesavaswamy at Bagur
in the Hosadrug Sub Taluk with a
sketch shewing the temple premises and
the portions to be repaired as called
for in the above.

Yours obedient servant

Deputy Commissioner

BS

Read again :—

Govt. Ro: No. 312-3 of 20th Sept. 1894 sanctioning an Estimate for Rs 1663-6 to repair the temple of Sri Chamakesavaswami at Bagur in the Hoodwga Sub Taluk.

And. Read. Correspondence ending with Docket No. 323/15 of 12th October 1898 from the Dy Commr. Chitaldrug Dt reporting, with an expression of regret, that the repairs sanctioned in the above order of Govt. have not been executed for want of a suitable contractor to undertake the repairs and other causes

Submitted

a revised Estimate
amounting to Rs ~~2106~~ 3769.
for the repairs of the Inst.n
providing therein for certain
additional works
since found necessary. Rs 675-6
8.12.98
En 4 & 2.

Order thereon

Under the circs
reported by the Dy Commr.,
the revised Estimate
for Rs ~~2106~~ 3769 is sanctioned,
the charge being met
as follows:—

Rs 393-12-10 being the amount available
at the credit of the temple
as per Treasury Officer's certificate
of 24th March 1898.

Rs 500-... being the contribution reported
to have been paid by the devotees
into the Holalkere Taluk Treasury
for the purpose of the temple repairs

Rs ~~1212-3-2~~ 2-2 from the State Grant
2875-3-2 of Rs 15000 - ~~Sanctioned~~
for repairs of Muzrai
buildings during 1898-9.

Total Rs ~~2607-~~ 3769/-

2. The Compt.r will be requested to place the ~~State Grant~~ of Rs 2875-3-2 ~~Sanctioned~~ in the foregoing para at the disposal of the Dy Commr.r Chitaldrug Dt.

3. The original Estimate for Rs 1663 ~~Sanctioned~~ in the Govt. order of the 20th Sept 94. read above is hereby cancelled.

Mysore Secy.

To.
The Dy Commr.
Chitaldrug Dt. with the Sanctd. Revd. Estt.
" Compt. Mysore Govt.
with Copy of the Hobli Revd

1900. 1901

FROM The Deputy Commissioner
Chitaldroog district

To The Secretary to the Govt of Mysore
Munpri Department
Bangalore

Dated 13th
Despatched } September 1900.
Received

General No. 2404
No.

Enclosure No. 3.



Submitting for sanction a finally revised estimate amounting to Rs 75-5-7/- for restoring and improving the Sri Chennakesava Temple at Bagur in the Hosdroog Sub-Taluk

Vide no 611 dt 3, 12/00

No: 244.
Cu: 3.

Office of the Deputy Commissioner
Chitaldroog District.

Dated. Chitaldroog 13th September 1900

From

The Deputy Commissioner
Chitaldroog District.

To

The Secretary to the Government
of Mysore, Muzarayi Department,
Bangalore

Sir,

With reference to Proceedings of Government no. 675-6 dated 8th December 1898, I have the honor to forward a finally revised estimate amounting to Rs 7,557/- for restoring and improving the Sri Chennakesava Temple at Baguri in the Hosadrooga Sub-Taluk.

2. A Comparative Statement showing the difference between the estimate sanctioned in 1898 and the one now sent and the reasons for the several variations is also herewith sent. In the Course of the execution of work, the additional work now proposed was found absolutely necessary, and the whole work is now very nearly

Completed

Completed. Owing to the exceptional circumstances of last year, I had no time to write for and obtain formal sanction to the variations before they were carried out

3. Out of the estimate sanctioned in December 1898, a sum of Rs 893-12-10. was available from amount at credit of the temple and from Contributions paid by votaries, and the balance of Rs 2,875-3-2 was sanctioned from the State grant. A further sum of Rs 3,788/10 now wanted, and out of this, a sum of Rs 80/- from funds available at credit of the temple and a sum of 100 Rs paid since by votaries as further Contribution have to be deducted. The balance of Rs 3608 has to be allotted from State grant

4. I am sorry the temple work has made a heavy demand upon State funds. When I assumed charge, I found the Concrete roofing of the whole temple had been removed. When replacing it, the greater part of the work carried out according to the final estimate was found necessary. There was therefore no alternative left but to finish the work to completion and I have been able to do in spite of great difficulties in this [illegible]

5. I beg the favour of

estimate now sent.

I have the [illegible]
Sir.
Your most obedient servant.

611

Madras

3

3rd Decr 1900.

To

The Dr Chelaldrug Dt

His Exc 2446 of 13th

Sept ao. Sanctg for Lumpsum

Amt Rs 755 7

for the repair & im-

provement of the

Sri Chenna Kesavaswa

Temple at Basur

Hoskote Taluk

in the modification

of the Estimate prd

Rs 3769 vacated

in Pro No. 675-6 of

8th Dec 1899 & cond

Sanctioning that the

works as per revised
Estimate now stated
have been nearly
carried out

It was the hope &
absence that it
was highly unfair
to have executed
works so large in
excess of the sanctioned
Estimate in
anticipation of
sanction to the
revised Estimate,
especially seeing
that the Temple
has no funds

Dr under the large
extra Cert. ~~Asst to~~
~~Rs 3~~. But before
however passing
final order on the
Petn, the Dr is
requested to report
at once, how much
of the allotment.
of Rs 3769 Sanct. ~~for the work~~
~~upon the temple~~
in the pet order of
the 8th Dec 98. has
been ~~already~~ drawn.
& what is in advance.
& expended ~~in the~~
on the repair of the Temple And. to ~~Enquire~~
measurement.
List for works also

already executed under the original Contract
in view to the adjustment
of the outstanding
advances. ~~between~~
~~any further allotments~~
~~case~~ 2- with reference
to the revised Estimate
now submitted for sanction
the Dy. C. requested
to report what
items of work
provided for therein
have been actually
carried out & at
what cost & what
items yet remain to
be executed
3. Enclosures Retd. herewith

Yours

(General Serial No. 30.)

1900 - 1901.



From The Deputy Commissioner Chitaldroog District

To The Secretary to the Government of Mysore Muzarai Department

Dated 20th } November 1900.
Despatched
Received

General No. 474 } 1900. 1901.
No.

Enclosures Number. 1.

Submitting his objections to Comptroller's objection slip No: 30 dated 20th September 1900 and requesting that fresh sanction to admit the charge of repairs to Chennakesavaswami temple at Bagur may be accorded.

To draw 1 report called for

Vide no 697 dy 8/1/01

No: 474. Office of the Deputy Commissioner
Ellis 10 Chitaldroog district.
Dated. Chitaldroog 30th November 1900

From.

The Deputy Commissioner
Chitaldroog District

To.

The Secretary to the Government
of Mysore –
Muzrai Department, Bangalore.

Sir.

I have the honor to submit herewith an original Comptroller's Objection slip No. 30 dated 20th September 1900, and to request that fresh sanction to admit the charge of repairs to Chennakesavaswami temple at Bagur, Hosadroog Sub-Taluk, for Rs 129 8-4-4 may kindly be accorded as requested by the Comptroller.

I have the honor to be
Sir,
Your most obedient Servant.

J W Hanumanthaiah
For Deputy Commissioner

MM.

MUZRAI

~~189~~ 1907

From

THE SECRETARY TO THE
GOVERNMENT OF MYSORE.

To

The Dy Commr
Chitaldrug Dt

Dated 8 January 1901

Despatched

Received

General No. 697
Muzrai F. No. /

Enclosure No.

His letter No 474 of 30 Nov 1900 requesting that sanction may be accorded to the adjustment, by debit to the State Grant provided in the current year's Muzrai Budget, of the sum of Rs 1298-4-4 drawn by him ~~for payment~~ and paid towards the cost of the repairs executed to the Sri Channa Kesavaswami temple at Bagur, Hosdurga Sub Taluk.

Has the honor to state that orders on the above will be passed on receipt of the information called for

in this Office Docket No. 611
of 3rd Dec. 1900, regarding
the extent of repairs already
executed to the Temple
and the total amount actually
drawn by the Dy Commr
for payment towards the cost
of the works. The Dy Commr
is accordingly requested
to expedite his reply to the
aforesaid reference.

By order

Asst

Mun Secy

Asst

MUZRAI

~~189~~ 1901

From

THE SECRETARY TO THE
GOVERNMENT OF MYSORE.

To The Comptr to Govt. -

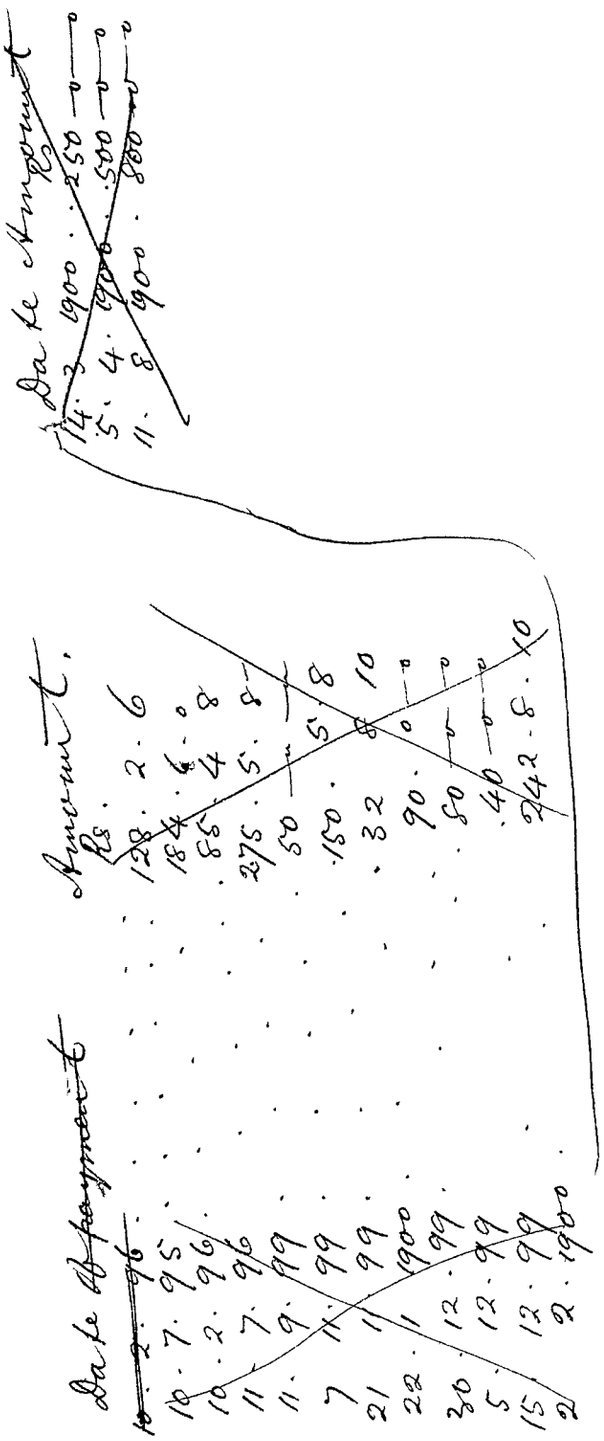

Dated 16th Feb

Despatched

Received

General No. 924
Muzrai F. No

Enclosure No.

In appending in the margin a Statement of the sums reported to have been drawn by the Deputy Comr. of the Chickballapur District, and paid towards the repairs of the Sri Chenna Kesavaswamy temple at Bagur, Hosdurga Sub. Taluk, as per Estimate sanctioned in the Govt Ro. No. 675-6, dated 8th December 1898, has the honor to enquire what payments are still outstanding in the accounts as advances pending adjustment and what payments have been

finally adjusted; In the case of the latter information is also requested as to the particular head to which each payment has been debited

By order,

Asst

Secy

Date	Amount
10 7 95	128 2 6
10 2 96	184 6 —
11 7 96	85 - 4 - 8 -
19 9 99	75 - — —
7 11 99	50 0 —
21 11 99	150 5 8
5 12 99	80 — —
15 12 99	40 - — —
30 12 99	90 — —
22 1 1900	32 - 8 10
2 2 1900	250 - — —
14 3 1900	500 — — —
5 4 1900	800 - — —
11 8 1900	132 4 —
11 8 1900	1166 - 0 4
	3764 - 0 - 0

Treasury Account Department.

(General Serial No. 30.)

13-3-01.

1901 / 812

From The Comptroller S.C.10 of Mysore.

To The Secretary to the Government of Mysore — Muzrai Department Bangalore

Dated 5th March 1901

Despatched 13

Received

General No. 4733 — 190 .

No. 1288.

Enclosures Number.

In reply to his no: 924 dated the 16th February 1901, has the honor to note in the margin the particulars of the amount drawn for the repairs to Chenna Keesavadeven temple at Bagur Chetta drug District and the heads to which they have been charged in the accounts of this office.

I have the honor to be, Sir, Your most obedient servant,

M Eagle

Assistant Accountant General.

Vide no 1017 dt 25-3-01

Remarks.

This Amount has been debited to "Receipts of Temples' Establishment" but still kept under objection pending receipt of explanation.

This Amount has been charged finally to 18 Muzrai Construction Repairs.

This has been finally charged to receipts of Temples.

The Amounts of these 5 items has been finally charged to 18 Muzrai Construction and repairs.

These 2 items are still under objection

Remarks	Vouchers	Amount.	
July 95.	279	128	2 6
February 96	242	182	6 "
July 1896	195	85.	4 8.
January 1899	182	365	" "
January 1900	348	152	14 6
February 1900	34	250	" "
March 1900	326	500	" "
April 1900	57	600	" "
August 1900	241	132.	4 "
"	298	1106.	" "
	Total	3764	" "

MUZRAI

1901

From

THE SECRETARY TO THE
GOVERNMENT OF MYSORE.

To

The Camp Vizag

Dated 25th March 1901

Despatched 26th

Received

General No. 1017

Muzrai F. No. 45-98

Enclosure No.

Ltr No 4733 of
1258

5-th March 1901

regarding the adjust-
-ment of the
Addams' dam
& the Dr w/ Vishaldra
Dr. for the repair
of the Dr Tank
Srirangapatna

MGCPB—11-1-1901—1500

Bapu. ~~Hodumpl~~
Hosdurga Tk Taluk
— a —.

Has the honor to
enquire why, art.
of the ~~items of~~
advances refd to
in the above, the
marginally noted
& 3 items ~~above~~
are 'under Objn'
& whether they have been
wholly
Charged in the
Accounts of ~~the~~
his Office.

Yours
Mukz. Secy

P/128-2-6 Accts Corrections. 279 of 1905.
" 132-4-0.
" 1166-0-4 .....

Engr. Hqrs
24th Feby 1906
298 of Feby 1906

23/4/01

661

No. 1456 5487

OFFICE OF THE COMPTROLLER OF MYSORE

Bangalore, 15th April 1901.

23 8/12

From

E. R. SUBRAYER, Esq.,

Comptroller, Mysore Government

To

The Secretary to the Govt. of Mysore,

Huzroi Dept

Sir,

With reference to the Huzroi Secretary's No. 1017 dated 25th Ultimo, I have the honor to state that the three items therein referred to have been provisionally adjusted in the accounts of this office by debit to the heads noted against them.

Voucher	Amount	Head to which charged	
279 for July 95	128-2-6	Public Debt	Receipt of Bond s.
241 for August 00	132-4-0	18 Huzroi 3 Construction and repairs	
298 for ,, 00	1166-0-4	Pending resanction of Power to accept the debit to S[illegible] be given.	

clearance pending the receipt of completion bills which I request you will be so good as to obtain and forward at an early date.

I have the honor to be

Sir

Your most obedient servant,

Comptroller.

D/128-2-6 Bills for Vouchers 279 &c.

Gen 30]

189

From

E R SUBRAYER, Esq.

Comptroller, Mysore Govt.

To

The Secretary to the Govt of Mysore,

____ *Dept.*

Dated

Despatched

Received

General No.

No.

Enclosure No.

In reply to

SUBJECT.

References (to be entered only in the Dewan's Office).

~~189~~ 1900 - 1901.

FROM The Deputy Commissioner Chitaldroog District.

To The Secretary to the Government of Mysore Muzarai Department.

Dated 25th January 1901.
Despatched
Received

General No. 608.
No.

Enclosure No. 29.

OF THE DEWAN OF MYSORE
RECEIVED
Date 4-99
REG. No. 422-01
MUZRAI BRANCH

Vide no 4 dt 1/2/01

Ex 25/1/01

Report

by

What are to clerus how to be adjusted?

Ans

Sahib.

The clerus to be adjusted are :-

Rs 128-2-6 as per bill I. Vide list of outstanding advances Ass Comptr

Rs 132-4-0 9
Rs 1166-0-4 . . . 10 & 11 } drawn by Dy. in Aug'00 but placed under objection by Comptr. ~~to be debited to Temple Fund~~ Vide Dy's No 474-B 20/9/00

(a) to be debited to Muzrai Temple Fund to current year's stamp. The other payments have been adjusted Ass. I. 1 2/07

Stating that major portion of the work provided in the revised estimate for the repairs of Sri Chenna-keswaswami temple at Bagur, in the Hosadroog Sub-Taluk has been already executed and submitting measurement bills and vouchers in support of the same.

Vide no 4 dt 1/2/01

Com Muzrai Dept to adjust as per remarks of Asst Comptr

Ans 12/2/01

No: 608. Ex: 29. Office of the Deputy Commissioner
Chitaldroog District

Dated, Chitaldroog 25th January 1901

From

The Deputy Commissioner
Chitaldroog District.

To

The Secretary to the Government
of Mysore. Muzarai Department,
Bangalore

Sir,

With reference to your No. 611 dated 4th December 1900, requesting me to report the amount drawn in advance out of the allotment of Rs 3,769/- sanctioned in Government Proceedings — No 675-6 dated 8th December 98, and expended on the repair of the Sri Chennakesava-swami temple at Bagur, Hosadroog Sub. Taluk, and to submit measurement bills for works already executed for adjustment of the outstanding advances, I have the honor to state that a sum of Rs 3,764/- has been drawn in advance and expended on the repairs of the said temple and measurement bills with vouchers in support of the charges are submitted

ao

as noted in the margin

2 As regards para 2 of the docket under reply, I beg to add that more than 90 per cent of the work provided for in the revised estimate has been executed, but it has not been measured and paced for for want of funds The measurements of works actually done up to date are being taken and the details will be furnished as soon as they are furnished to this office In the meantime, it may roughly be stated that the following items of work remain to be done (1) Plastering walls and over Concrete (2) Pointing Compound wall (3) Fixing Coping slabs over the same (4) Repairs to floor and (5) Preparation of doors and windows.

3 The enclosures are herewith returned

I have the honor to be
Sir,
Your most obedient Servant,

For Deputy Commissioner

~~189~~ 1901 C. 1



FROM The Deputy Commissioner
Chitaldrug Lestrict

To The Deputy Secretary to the
Government of Mysore

Dated 26th June 1901 Bangalore
Despatched
Received
General No. 1076
No.

Enclosure No. "—

Refers
Rs
28/6/01

With reference to this office
No 608, dated 22nd January last,
regarding repairs and improvements
to Sri Chennakesavaswami ↪
temple at Bagur, Hosdrug Sub-
Taluk, has the honor to state
that for want of sanction to the
revised estimate submitted with
this office letter No 2424, dated 12th
September last, the proofing of a
portion of the main temple and
of the Southern Mantapam ↪
remains unfinished, although the
materials for the same have been
collected. The buildings in their
present condition, present a very
dilapidated appearance, and
they cannot be allowed to ↪
continue any longer in that
condition; more especially a

Vide No 53-4 of 8.7.01

the rainy season has set in. The contractor cannot be further induced to execute this item of work also in anticipation of payment, as he has already spent on the work a large amount, which has to be paid for by Government.

Request therefore that Government will be pleased to accord sanction to the revised estimate, above referred to, at an early date.

[illegible]

For Deputy Commissioner

Mysore.

Read:— Govt. Pro No. 675-6
Mus 745-98
of 8th December 1898 sanctioning
a revised Estimate for Rs. 3769
for repairing the Sri Channa
Kesavaswami temple at
Bagur in the Hosdurga Sub Taluk.

And:— Correspondence ending
with letter No 608 of 25th
from the Dy Commr Chitaldrug Dt—
January 1901, reporting
on the repairs of the temple.

Order thereon.

No. 53-4.
Mus 745-98
D/ 8/7/01
Enc 11 Bills & Vouchers

The Dy Commr reports that in the course of the execution of the repairs sanctioned in the Govt. Pro. read above, certain additional works were found absolutely necessary, that certain variations in the items of work provided for

the Revised Estimate had
to be made that a sum
of Rs 3764- has been drawn
in advance and expended
on the repairs of the Instn, and
that out of this amount,
Rs 1298-4-4 was not
drawn within the close
of the year in which it
was sanctioned out of
the State Grants and requesting
therefore fresh sanction
to admit the charge brought
under objection by the
Comptroller; and submits
for Countersignature measurement
Bills with Vouchers amounting
~~aggregating~~
to Rs 3764- on account
of works executed.

2.

The Measurement

Bills aggregating to Rs 3764- are Countersigned and forwarded to the Compt.r for adjustment of the advances drawn by the Deputy Commissioner on Vouchers accompanying the Bills. The sum of Rs 1298-4-4 which was not drawn within the year of its sanction will be met from the State Grant of Rs 15000- provided during the year 1901-1902.

3. The Dy Commr will be requested to submit for sanction a Supplemental Estimate for such other items of works as ~~have~~ have been already executed in anticipation of sanction.

~~Completed~~

1	Rs	128-2-6
2	"	184-10-0
3	"	85-4-8
4	"	275-5-0
5	"	242-8-10
6	"	250-0-0
7	"	800-0-0
8	"	880-0-0
9	"	132-4-0
10	"	1166-0-0
		Total Rs 3764.

The Govt. however Observe
that it was highly irregular
to have executed works
so largely in anticipation
of Sanction especially
seeing that the Temple
had no funds of its own
to bear the Cost.

LL
6/7/01
Dy Secretary

To, The Dy Commr
Chitaldrug Dt.

" Compt. ellysore Govt. with the
Measurement-Bills & Vouchers.

Gen. 31]

~~189~~ 1902.



From M. Narain Rao Esquire
Deputy Commissioner
Chital drug district.

To L. Ananthasami Rao Esqre.
Deputy Secretary B.A. to the
Govt. of Mysore -
Muzrai Department

Dated 28th February 1902.

Despatched

Received

General No. 728.
No.

Enclosure No. 2.

Soliciting early sanction
to the supplemental estimate
amounting to Rs. 3251/- for
repairs to be done to Sri Channa-
Kesavaswamy's temple at —
Balur, Hosdurg Sub-Taluk.

Refers
Rs
3/3/02

Note contd &
Subpd proceds
5/3/02

Vide no 2002-3 dt 6/6/02

Deputy Commissioner's Office
Chittaldrug District
No. 728 Enc 2
Dated 28th February 1902

From

M. Narain Rao Esquire
Deputy Commissioner

To

L. Ananthasami Rao Esquire
Deputy Secretary Mysore
Department

Sir

With reference to para
3 of Proceedings of Government
No 53-4 / Revs 7145-98 Dated 8th July 1901,
I have the honor to submit a
comparative statement
shewing the difference between
the Sanctioned Estimate

and the work executed upto to date from which it will be seen that against the sanctioned Estimate of =Rs 3769, work of the value of =Rs 4,564-1-5 has actually been carried out, for which Rs 3769 has been paid to the Contractor and =Rs 795-1 5 still remains to be paid

2. A Supplemental Estimate amounting to =Rs 3,251 for work remaining to be done to the temple in order to complete the repairs, is submitted for sanction. I have inspected the temple more than once and consider these works essential. Some of the items provided for in the Supplemental Estimate were taken in hand and materials

Maitland Park collected before I
assumed charge of the District,
but work has been suspended
since July 1901 It is necessary
that the Concrete roofing
should be finished before
the Monsoon sets in, and I beg
to request that early Sanction
may be accorded to the Supplemental
Estimate herewith forwarded.

I have the honor to be
Sir
Your most obedient Servt
M Nanavati Esq
Dy Commissioner

Muzrai.

Read:- 817

Govt. Pro. No. 53—4 Muz 7 45-98 dated 8th July 1901, Counter-signing and forwarding to the Compt. for adjustment, measurement bills aggregating Rs 3764/- on account of the repairs executed to the Sri Channa Kesavaswami temple at Bagur in the Hosdurga Sub Taluk.

And,

Letter No. 728 dy 28th February 1902, from the Dy Commr., Chitaldrug District, reporting in regard to the four

repairs needed to the
Institution

Order thereon Nil

No. 2002-3 En
Irrig. F. 45-98

In his letter read above, Dy 6/6/1902
the Dy Commr, reports
that against the Sanctioned
Estimate amounting
to Rs 3769, works of the
value of Rs 4564-1-5
have actually been carried
out, for which a sum
of Rs 3769 has been paid
to the Contractor ~~as per~~
~~measurement bills passed~~
~~in the Govt. order read above~~,
and that Rs 795-1-5
still remains to be paid.

The Dy Commr. also submits for sanction a supplemental Estimate amounting to Rs 3251/- for works still required to be executed to the temple

2. With reference to the above, the Govt. observe that for work actually executed, a further sum of Rs 795-1-5 is still due. This amount is sanctioned from the State grant of Rs 15000/- provided in the current years' Muzrai Budget. The Comptr is requested to place the amount

at the disposal of the
Dy Commr for payment.

3) In regard to the further
repairs to the temple,
the Dy Commr is requested
not to start any more
work without obtaining
previous sanction. The supplemental
~~revised~~ Estimate is returned
herewith unsanctioned.
The Dy Commr is requested
to report what are the items
of work that have been executed
& what are the items that have
yet to be done. If the latter are
not of an urgent nature, they
cannot be undertaken now as
much money has been already spent
on this temple without due authority

Dft 6/14/12

Dy Secretary
Revs: Deptt

To the Dy Commr Chitaldrug Dist for the suppl Estimate Vendor
" DSPWI

1902



8/9/02

QA

Please check & bring up

ks
8/9/02

Note Contd & submd

ks
13/9/02

From
M. Narain Rao Esquire
Deputy Commissioner,
Chitaldrug District

To
H. V. Nanjundayya Esquire MA, ML.
Secretary to the Government
of Mysore — General and
Revenue Departments,
Bangalore

Dated 4th September 1902

Despatched

Received

General No. 188
No.

Enclosure No. 4

Submitting Explanatory Memoranda shewing the work done to Sri Chennakesava Swamy temple at Bagur in the Hoskote Taluk of this District together with that remaining to be done to complete the repairs undertaken —

Bangalore
9/9/02

70

Office of the Deputy Commissioner,
Chitaldrug District.

No 188/Rne 4

Dated, Chitaldrug 4th September 1902

From

M. Narain Rao Esquire,
Deputy Commissioner,
Chitaldrug District.

To

L. Ananthasami Rao Esquire B.A.
Deputy Secretary to the Government
of Mysore, Muzrai Department,
Bangalore.

Sir,

Adverting to Government Proceedings No: 2002-3 Muz.F.45-98 dated the 6th June 1902, I have the honor to submit herewith Explanatory Memoranda A and B shewing the work already done to the Sri Chenna Keswaswami temple at Bagur in the Hosadurga Taluk (Rs 4564-1-5) and that remaining to be done to Complete the repairs undertaken.

2. A Supplemental estimate for Rs 3137/— is herewith forwarded for Sanction, providing for works which it is considered essential in order to Complete the repairs. I have seen the temple and satisfied myself that the works herein provided for are necessary.

I have the honor to be,
Sir,
Your most obedient Servant,

M Narain Rao

Deputy Commissioner,
Chitaldrug District.

Dn

A

Memorandum showing the items of work already executed in repairing Sri Chennakeswaswami's Temple at Bagur in the Hosadurga Taluk

Work done Rs 843-9-"

I Concrete Work.

New Concrete has been put over the Northern Mantap Yagasala, the front Verandah and a portion of Southern Mantap

Work done Rs 42-3-10

II Dismantling old Concrete.

Old Concrete has been wholly removed, measurements taken and payment made

Work done Rs 70-"-"

III Dismantling and [illegible].

A portion of the wall of the main temple which was in a very dangerous State has been dismantled and rebuilt

Work done Rs 51-10-"

IV Dismantling brick [illegible].

Walls of Northern Mantap, Yagasala, front Verandah Mahadwara, and Southern Mantap which [illegible]

a dilapidated state were dismantled
he and the Cost debited to this sub head

V Brick in Chunam — Work done Rs 2241-7-9

Levelling the uneven portions of slabbed roof, Construction of a portion of the parapet wall on the roof of the Mantapas and erection of walls of the Southern Kacsala, formation of rooms on both sides of Mahadwara have been done and the outlay debited to this sub-head

VI Plastering with Chunam. — Work done Rs 207-7-11

Vide explanation under the Sub-heads "Concrete" and Brick in Chunam:

VII Earthwork. — Work done Rs 9-15-6

Excavation of foundation for the walls above referred to and the Compound wall on the left side has been done

VIII Roughstone in Clay. — Work done Rs 301-10-8,

Compound wall on the left side has been Constructed

IX Burnt stone slabs dressed and fitted — Work done Rs 20-13-9

For Lintles over doors and windows

Work done
Rs 36-"-"

X Teakwood [illegible] door.

2 doors have been fixed to the Yagasala.

Work done
Rs 30-"-"

XI Removal of [illegible]

The clay and mud over the Covering slabs instead of Concrete was removed.

Work done
Rs 46-"-"

XII Adding one Arkan [illegible]

One Arkanam had Collapsed and this was newly put up

Work done
Rs 88-12-"

XIII. Roughstone in [illegible]

The walls of the main temple were formerly Constructed with thick slabs and interspaces filled with mud. The mud was removed and the space filled up with roughstone in Chunam in places

Work done
Rs 475-5-6

XIV Stone in [illegible]

Foundation of walls of Southern Mantap and a pillar to support a broken girder in the front Verandah was Constructed.

Work done
Rs 93-7-6

XV [illegible]

498½ Square feet of slabs laid in [illegible]

Collected 41 These are required for Coping
over the Compound wall

XVI Mud-plastering. Work done
Rs 5-10-11

This was done to the Screen
walls of Yagasala

M. Narain Rao
Deputy Commissioner
Central drug District.

DN

B

Explanatory memo showing the items of work left to be done as per Supplemental estimate for repairing Sri Channa Kesava Swamy's temple at Bagur in the Hosdurga Taluk

I Concrete work

work done - 4908 C. ft.
work remaining to be done } 3814 Do

A portion of the roof of Southern line of Kansale Mantap and that of the whole of the main temple was dismantled more than a year ago as it was in a leaky State and materials necessary to put on new concrete have been collected. These items were ordered by Mr. M. S. Narayana Rao, Deputy Commissioner, in addition to those provided in the Sanctioned estimate. The dismantled roof must be covered over with new concrete. The item of 3814 Cubic feet provided in the Supplemental estimate is therefore essential.

II. Teakwood doors 5½ in Nos

amt provided estimate Rs 204
work done "
work to be done " 276

Nine of the doors now in the temple is serviceable. Four doors to the main temple, 1 door to the Lakshmidevi temple and 1 door to the Ganapathy Swami temple as well as 4 windows in the walls of the main temple and 4 windows to the Chimney proposed to be built in the main temple are provided for in the Supplemental estimate. The Sanctioned estimate provided for only 6 doors at a cost of Rs 204/. The Chimney and windows are considered essential to admit of more light and air into the main temple

Brick [illegible]

Work done 4317
Work to be done 4051

No Provision under this head is made to build parapet-walls on the southern line of Kausale and on portions of the main temple and to effect urgent repairs of roof covered by slabs where new concrete has to be used. Rear wall of Alvar temple has also to be re-built, as the present one is in a dilapidated condition and may come down any moment. These works are indispensable

[illegible]

Vide explanation under concrete and brick-in-chunam.

See estimate for 5-
Work done 207
To be done —

[illegible]

The space on the right-side of the temple was only proposed to be walled up, but the mud wall of the left-side compound having come down, its re-construction has become necessary

See estimate No 135
Work done 284
To be done 151

VI [illegible]

Nil

One of the stone girders in the front-verandah was found to have been broken and a pillar with burnt-stone in chunam-had to be constructed to guard against further danger. A similar pillar on the left-side is very necessary to preserve symmetry and cannot therefore be dispensed with.

A wall on the southern side of the Alvar devastan-has to be built. The old wall is in a dilapidated condition

VII Burnt Stone Slabs dressed and fitted

See estimate No 152
Work done
To be done 265

Coping-slabs over compound wall are very necessary for the safety of

of the wall are to be built with roughly dressed stones in clay. The required number of slabs have already been collected and part payment made for collection dressing and fixing them on the wall alone remains to be done

VIII [illegible] hours

Some rooms have been formed in the northern and southern entrance and on both the sides of main hardware for the use of pilgrims. It is undesirable that they should be left without doors and windows since the pronaos. Requisite materials have all been collected and frames prepared

IX [illegible] fence

The pronaos is made for a gate all the main hardware are to be fixed on the top

Sanctioned estimate Rs 50
Work done Nil
Work to be done 50

Sanctioned estimate Rs 92
Work done Nil
Work to be done 92

rough pounded wall built with stone in clay and not to be left without pointing the joints with mortar

New provision Rs 200

X. [illegible]

Side walls

The side and front walls in the temple were formerly built with the dressed slabs but without proper bond. Consequently, many portions had come to grief. The repairs of these portions have been attended under the orders of [illegible] Shri Jha and Gupta [illegible] have to be made after the rainy season [illegible]

New provision Rs 38

[illegible] the repairs [illegible] garud a temple [illegible] part

is in a dilapidated state, & is early repair is necessary.

New provision Rs 30/-

~~Extension of the existing verandah in front of the entrance to the Chief Judge's Court.~~

As the halls of the main temple are very dark, this arrangement is proposed. The cost is not great.

New provision Rs.

~~Extension of the doors in the walls of the Court of the Chief Judge.~~

Vide explanation under the above sub-head. Rs 12-0-0

Chittaldrug
4th Sept 1902

Dy

Mahamad Rao
Deputy Commissioner

Govt and

3. The Supplemental Estimate accordingly returned herewith unsanctioned, with the remark that, if the Dy Commr. will send up a small Estimate for such of the works as are actually required to make secure those actually already done to the Mattr., the proposal will be considered by Govt., and not otherwise.

By order,

25/9/02

Dy Secretary

Muz: Deptt.

JS

MUZRAI

1902-03

From Dy

THE SECRETARY TO THE GOVERNMENT OF MYSORE

To

The Deputy Commr.,
Chitaldrug Dt.

Dated 29th Sept. 1902.

Despatched

Received

General No. 620

Muzrai F. No. 45-98

Enclosure No. 1

His letter No 188 dated 4th September 1902, submitting for sanction a Supplemental Estimate amounting to —

Rs 3137/- for further repairs to the Sri Chenna Kesavaswami Temple at Bagur, Hosadurga Taluk

——"——

Has the honor to state that works to the extent of Rs 4564-- have been already executed to the Sri Chenna Kesavaswami Temple at Bagur

paid for, Rs 3670-4-7 thereof having been met from the State Grant.

2. The Deputy Commr. now submits with the communication cited above a Supplemental Estimate amounting to Rs 3137/- for certain additional repairs to the temple, and requests that this amount may also be paid from the State Grant of the current Fl. year. With refce to this, the Deputy Commr. is informed that it is not possible to give such a large grant to this one temple alone, this year. The State Grant is not intended to serve the purposes of merely one or two Institutions in the State, but of all that are in need of

1902

FROM
M. Varadaraja Rao Esquire,
Deputy Commissioner,
Chitaldrug District

To
L. Narasimha Rao Esqre. BA
Deputy Secretary to the Govern-
-ment of His High ness the
Maharaja of Mysore,
Mulki department

Dated 21st
Despatched 23rd
Received
Bangalore
December 1902

General No. 489
No.



Enclosure No. 7
(Plan Sent Separately)

His No 620 dated 29th September 1902, returning for re-Submission of a smaller estimate the Supplemental estimate for repairing Sri Chennakesavaswamy's temple at Bagur in the Hosdurg Taluk. 45-98

With reference to the above, I have the honor to submit a plan and a detailed estimate of the items of works which are found to be absolutely necessary both to secure the safety of the works already executed, and also to ensure the stability of the building in general.

Muz (Fr)

27/1-/03

Subject with the Minor notes contained therein.

W. 13.1.03

2 There is an increase of Rs 56/ under brick in Chunnam as compared with the provision made in the previous Supplemental estimate under that head, but this has been necessitated on account of the new arm temple which forms part of the Southern Kysala, which is in a very dilapidated condition. Unless that portion of the temple is also put in repair, the general appearance of the structure will be spoilt.

Mr Narain Rao
Deputy Commissioner

1903

From H. Ramanujaiengar Esquire
Deputy Commissioner
~~Chitaldroog~~ Tumkur

To L. Ananthasami Rao Esqr B.A.
Deputy Secretary to the Government of Mysore, Muzrai Department,

Dated 29th Bangalore
Despatched November 1903
Received Camp Davangere

~~General~~ Camp No. 94
No.

Enclosure No. —

Requesting Early Sanction to the Supplemental estimate submitted with this office No. 489 dated 21/23 Dt Instant for certain work remaining to be done to the Chennakesava Swami Temple at Bagur in the Hosadurga Taluk.

Read
30/11/03
Rs

Submitted to the Dy Secretary in continuation
Rs
2/12/03

Camp No: 94

Office of the Deputy Commissioner,
Chitaldrug District.

Dated, ~~Chitaldrug~~ Camp Davangere 29th November 1903

H. RAMANUJA AIYANGAR Esqr
Deputy Commissioner,
Chitaldrug District.

To L. Anantha Rama Rao Esquire B.A.
Deputy Secretary to the Government of
His Highness the Maharaja of Mysore,
Muzrai Department,
Bangalore

Sir,

Adverting to this office No: 489 dated 21/23d instant, submitting for sanction a plan and supplemental Estimate for repairing the Temple of Sri Chennakesava Swami at Bagur in the Hosadurga Taluk, I have the honor to state that I inspected the temple on the 16th instant. Notwithstanding the large sum spent on the work, the temple presents a very incomplete appearance, to say nothing of the gradual deterioration which it has since undergone. More money has been spent on the out-houses than on the main building. The further work provided for in the supplemental estimate is urgently necessary and

and I therefore request that it may be
kindly sanctioned as early as convenient.

I have the honor to be,
Sir,
Your most obedient Servant,

D. R. Williamson
Deputy Commissioner
Civil Engineering Dept.

MYSORE CO... 1622 MUZRAI SECTT...

Rec'd 2/2/04

Sent both in Contn

2/2/04

1904

From A. Ramanujacharyar Esqr
Deputy Commissioner
Chitaldrug Division

To L. Ananthasami Rao Esqr B.A.
Deputy Secretary to the Government of
His Highness the Maharaja of Mysore,
Muzrai Department.

Dated 30th Bangalore.
Despatched 1-2 January 1904
Received

General No. 4664
No.

Enclosure No.

This Office Camp No. 94 dated 29th November last, submitting for sanction a plan and supplemental Estimate for repairing the temple of Sri Chennakesavaswamy at Baguru in the Hosadurga Taluk

Has the honor to invite Kind reference to the above and to request an early reply thereto

Dy Deputy Commissioner
Chitaldrug

MUZRAI SECRETARIAT.

1903 - 1904

S.C. 9.3

From H. Shama Rao Esqr. M.A.,
~~L. ANANTASAMI RAO, Esq., B.A.,~~
Deputy Secretary to the Govt. of
H. H. the Maharaja of Mysore,
Muzrai Department.

To The Dy Commissioner
Chitaldrug District

Dated 14th } April '04.
Despatched 14th }

Received

General No. 3243
Muzrai F. No. 45-98

Enclosure No. (2) { 1. Estimate
2 Plan
(Sent separately)

His letter No. 489 dated 21st December 1902 submitting for sanction an estimate amounting to Rs 2830 for repairing the Sri Channakesavaswami temple at Bagur in the Hosadurga Taluk and the marginally noted ~~noted~~ ✕ reminders thereto.

Referring to the above, I have the honor to enquire what

✕ No. 94 dt: 29.11.03
" 404 dt: 30.12.03

particular
(works) are absolutely necessary
and what the probable cost
of each of the works, would
be.

2 The plan and the supple-
mental estimate received
with the above are herewith
returned.

By order
Leo. W. W. 04

(Dennis order)

Secretary

Rs
13/4/04

MYSORE GOVERNMENT
3244
MUZRAI SECRETARIAT

1904

From

H Ramanujachyangar Esqre
Deputy Commissioner
Chitaldrug District

To

M Srinivasa Rao Esqre Acting
Offg Secretary to the Government
of His Highness the Maharaja
of Mysore, Religious Department

Dated Bangalore

Despatched 15/6 } June 1904

Received

General No. 648

No.

Enclosure No.

15/6/04

EA

Requesting sanction of Government to the estimate for repairing the Chenna Kesawaswamy's temple at Bagur in the Hosadurga Taluk.

No 648
Genl 2

Deputy Commissioner's Office
Chitaldrug District
Dated Chitaldrug 14th June 1902

From

N. Ramanujacengar Esquire
Deputy Commissioner
Chitaldrug District

To

The Shama Rao Esquire M A
Ag Secretary to the Government of
His Highness the Maharaja of Mysore,
Mazrai Department,
Bangalore.

Sir,

In acknowledging receipt of your docket No 3243/45-98 of the 14th ult Genl, I have the honor to state that I have personally inspected Sri Chennakesava swamy temple at Bagur and satisfied myself that every provision made in the supplemental estimate re-transmitted herewith is very essential. The repairs to the surrounding buildings are yet incomplete and their early completion is highly desirable. No repairs have been executed to the main temple with the exception of dismantling concrete over the slabbed roof and it has been left in this state for more than 5 years, all the rain wat-

to this allowed to find its way into and absorb in the main temple The requisite material for the completion of all these works have been made ready as per personal order of Col. H. Narayana Rao the then Deputy Commissioner Hence it seems to me hazardous at this stage in that to reduce or alter or with any of the items of works provided in the supplemental estimate

2 Under these circumstances, I beg that you will kindly obtain the sanction of Government to the estimate herewith submitted The plan also accompanies

I have the honour to be

Sir

Your most obedient servant

K. Chamaraja Wadiyar

MUZRAI SECRETARIAT.

190 —190 98.1

From

L. ANANTASAMI RAO, Esq., B.A.,
~~Deputy~~ Secretary to the Govt. of
H. H. the Maharaja of Mysore,
Muzrai Department.

To

The Deputy Commr.,
Chitaldrug District

Dated 5th July 1904.

Despatched

Received

General No. 98
Muzrai F. No. 45-98

Enclosure No. (2)

With reference to his letter No. 648, dated the 4th June 1904, reporting that the Supplemental Estimate for Rs 2830/- submitted by him for the repairs of the Sri Chenna-Kesavaswami temple at Bagur in the Hosadurga Sub Taluk, provides for the completion of the repairs to the buildings around the temple and for the repairs of the main temple, the concrete over the slabbed roof of which had been dismantled, ~~now~~ has the honor to request to be informed as to the practicable

MGCPL—1000-21-1-04

cost of executing each of the items of above, Repairs, as called for in this Office No 3243 Mus 45-98, dated the 14th April 1904.

2. Inquired further whether it would not be sufficient to confine the Repairs for the present to the main Temple alone, and if so, what the cost of that work alone will amount to.

3. An early reply is requested.

4. Envs noted for rep & return

By order,

3/7/04

Secretary
Mus. Deptt.

1/7/04

MYSORE GOVERNMENT
495
MUSEUM

1904

From H Ramanuja Iyengar Esqre
Deputy Commissioner
Chitaldrug District

To L. Anantasami Rao Esqre
Secretary to the Government of
H.H. the Maharaja of Mysore
Dated 27th Mugalvi Department
Despatched 28th July 1904. Bangalore
Received
General No. 63.
No.

Enclosure No. 3.

Submitting a report on the inspection of Sri Chenna Kesavaswamy's temple at Bagur in the Hiriyur Taluk — with three revised estimates for the repairs required for the temple.

ed
30/7/04

2 copies
Jas

No. 63 Encl 3

Deputy Commissioners' office
Chitaldrug District
Dated Camp Davangere 27th July 1904
28th

From

M. Ramanujaiengar Esquire
Deputy Commissioner,
Chitaldrug District

To

L. Anantasami Rao Esquire B.A.
Secretary to the Government of Mysore
Mujrai Department, Bangalore.

Sir,

With reference to your docket no 98/Muz 7 45-98 dated 4/5th Instant returning the supplemental Estimate for Rs 2830/- for the repairs of Sri Chenna Kesava-Swamy's temple at Bagur in the Hosadurga Taluk for resubmission with further information, I have the honor to state that I again inspected the temple on the 24th Instant and subjected every item of the Estimate to the most careful Scrutiny in consultation with the Dharmadarsis and others interested in the temple. I now submit herewith 3

Separate

Estimates amounting in all to Rs 1740/- in place of the original Estimate for Rs 283-/- and beg to state as follows: —

The 1st for Rs 1340/- is an Estimate for the repairs of the main temple. In this the work of dismantling and reconstructing the front and rear walls of dressed stones with the insertion of bond stones for which a lump sum of Rs 200/- has been provided, has already been executed; but the payment was withheld pending sanction to the Estimate. The roof of the main temple was dismantled more than 3 years ago as it was in a leaky state and materials necessary to put on new concrete have been collected. These items were ordered by Mr. M. S. Narayana Rao, the then Deputy Commissioner, in addition to those provided in the sanctioned Estimate. The dismantled roof must now be covered over —U—

new concrete, for which Rs 335/- have been provided. As none of the doors of the temple is serviceable and the substitution of fresh ones is considered essential, Rs 228/- have been provided for teak wood doors half battened and fully carved. A provision of Rs 325 is made to build parapet walls on the main temple and to level uneven portions of the roof covered by slabs where new concrete has to be used, which is also indispensable. This work has already been partly done. As the interior of the main temple is very dark, a lumpsum of Rs 50/- is provided for the construction of a sky-light in the Madhyaranga with 4 windows. Provision has also been made to fix 6 windows in the compartment next to the Garbhagudi so as to admit light and air which are now badly wanting.

The 2nd is an Estimate for Rs 175/- for the repairs of Southern Kapale attached to the temple which is at present in an incomplete state. Its roof was dis-mantled more than 3 years ago, and it was intended to cover it with fresh concrete. As the cost of this would be rather heavy, I have dispensed with this item and substituted clay. A provision of Rs 97 under "brick in chunam" is made to level uneven portions of the roof covered by slabs, and this work has already been carried out.

The 3d is an Estimate for Rs 225/- for the construction of the Compound wall and plastering over the concrete roof of Mahadwara. The wall was constructed more than 6 years ago with rough stones in clay and the cost debited to the original Estimate,

Coping with burnt stone slabs and pointing the joints with Chunam still remain to be done. As these works require more than Rs 350/- they have been dispensed with and Coping with mortar and burnt stone chips substituted and the cost reduced to Rs 111. The Mahadwara or the entrance has stone frames but no shutters, without which the temple does not present a decent appearance; and moreover stray cattle cannot be kept out

I beg that you will kindly move the Government to accord sanction to the reduced Estimates now submitted. The plan also accompanies.

I have the honor to be,
Sir,
your most obedient Servant

Deputy Commissioner
Chittagong District

Muzrai

Read:-

Correspondence ending with letter no 63, dated 28th July 1904, from the Dy Commissioner, Chitaldrug Dt, submitting for sanction three revised estimates aggregating Rs 1740/- as noted in the margin for completing the repairs of the Sri Chennakesavaswami temple at Bagur, in Hoodruga Taluk, and reporting that these estimates have been prepared after the most careful scrutiny and in consultation with the Dharmadarsis and others interested in the institution.

For Repairing the main temple .. Rs 1340/-
" Kyasalé " 175/-
" Compound wall " 225/-
Total Rs 1740/-

Order thereon no:
869-70 Revenue 4+3 Dt 31/8/04-
M: 7: 45-98

The estimates aggregating Rs 1740/- are sanctioned, the charge being met from the State Grant of Rs 15,000/- provided in the current year's Muzrai Budget

2. The Comptr to Govt will be requested to place the amount of the State Grant sanctioned.

bove at the disposal of the

Comm^r of the Chitaldrug Dist^t who

requested to draw the amount
unnecessarily
and credit it to the funds of the
All the works should be completed in an efficient manner
Inst^n &c before the close of the
and a report submitted to Govt.
current off.^l year, ~~so as not to~~

~~allow the same to lapse~~

3 The Dy Commissioner's attention

is drawn invited to the concluding

para of Govt Pro No 2389-97, Dy

30th May 1903, and he is requested

strictly
to refrain from undertaking any

further works from the State Grant,

without obtaining the previous sanction

of Govt in the Mysore Deptt

Dewan's order 27/8/04

Secretary,
Mys. Dept

To

The Dy Comm^r, Chitaldrug Dt
March 15th
returning the estimates ~~& correspdce~~.

a Compte, Mysore Govt, with copies of the
abstract Estimates

Keep copies of the abstract
of the Estimates
27/8/04
